Inspection Report





This inspection report prepared specifically for:

Antonio R & Ida Martinez Revocable Living Trust 1511 Dale Avenue Arroyo Grande, CA 93420



Inspected by: Gregory S. Terry

Table of Contents

General Information 1 Bathrooms 16
Roof
Exterior 2 Garage & Carport 19
Grounds & Drainage 4 Attic
Heating & Cooling 8 Foundation 22
Plumbing 10 Deficiency Summary
Electrical
Kitchen & Laundry 13

Copyright © 2017 New Image Software, Inc.™ All rights reserved. Rev 12/2015



		T INFORMATION

Report Date: 3/27/2017

Customer File # 14833

:

· Antonio R & Ida Martinez Revocable Living Trust

Address:

,

Phone: Fax: Fmail:

Inspection location: 1511 Dale Avenue

Send report to: Jeanne Salter

Help-U-Sell Town & Coastal

Arroyo Grande, CA 93420

Phone:

County: San Luis Obispo

Area/Neighborhood: Sub-division:

GENERAL INFORMATION

Main entry faces: North Bedrooms: 5 Full Baths: 2
Estimated Age: 38 Vehicle Garages: 2 Car Half Baths:
Type Structure: Single Family Home Approx. Sq Footage: 3/4 Baths: 1

Stories: 1

Type Foundation: Slab

Soil condition: Dry

Weather: Clear Temp: 60-70

Date: 3/27/2017 Time:

Unit occupied: yes Client present: yes

Attendees: Seller

General Overview:

Notice to 3rd parties or other purchasers: Receipt of this report by any purchasers of this property other than the above listed party(s) is not authorized. This report is prepared for the exclusive and sole use of the client listed above. This report is a work product and is copyrighted by the company listed above. Duplication by any means whatsoever is prohibited. Unauthorized duplication of, use or reliance of this report has the effect of all parties agreeing to hold harmless the inspector and the corporation.

Inspector:

Gregory S. Terry

REPORT LIMITATIONS

This report has been prepared for the use of the client indicated above is limited to an impartial opinion which is not a warranty that the items inspected are defect-free, or that latent or concealed defects may exist as of the date of this inspection or which may have existed in the past or may exist in the future. The report is limited to the components of the property which were visible to the inspector on the date of the inspection and his opinion of their condition at the time of the inspection.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 1 of 22

Roof

	COMPONENT CONDITION		ACTION RECOMMENDED	PERSPECTIVE
1	Roof coverings:	Most Acceptable	Repair - See Comments Below	Moderate
2	Ventilation:	Acceptable		
3	Flashings:	Most Acceptable	Repair - See Comments Below	Potential Leak
4	Skylights:	N/A		
5	Chimneys:	Most Acceptable	Repair - See Comments Below	Fire Safety
6	Gutter system:	Not Present	Repair - See Comments Below	Maintenance Item
7	:			
8	:			

	INFORMATION						
9	Main roof age: 10 Years Old (Estimate)	14	Ventilation: Eaves & Gables				
10	Other roof age:	15	Chimney: Metal (2)				
11	Inspection method: Walked entire roof	16	Chimney flue: Metal				
12	Roof covering: Fiberglass Shingle	17	Gutters: None				
13	Roofing layers: 1st	18	Roof Style: Gable				

ROOF COMMENTS

General Note: Our roof inspection is to report on the type and condition of the roofing material, missing and/or damaged materials and attachments. (Excluding ancillary items such as antennas, satellite dishes, solar panels, etc.) This does not constitute warranty, guarantee, roof certification or life expectancy evaluation of any kind. Roofs are not water tested for leaks. Condition of the roof underlayment is not visible and therefore cannot be evaluated. Structures that have concrete tiles, clay or wood shake/shingle materials that are going to be tented for fumigation are advised to be reinspected for damage caused after the tent is removed and prior to close of escrow.

Maintenance Note: Recommend installing gutters and down spouts to improve lot drainage. The down spouts should be extended to drain the surface water away from the perimeter of the foundation.

- 1.) There are no cricket flashing behind the chimney enclosures. This is required when the chimney enclosure is greater than 30 inches in width to divert water around the chimney. This may render these areas to potential leaks.
- 2.) Field shingles have been used for caps at the ridge line on the roof. This is an unconventional installation and may subject the ridge shingles to future wind damage particularly as the roof gets older.

Fire Safety Hazard Note: The spark arrestor is missing at the top of the family room fireplace and the spark arrestor is damaged at the top of the living room fireplace.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust


Page 2 of 22



Field shingles used for ridge caps on the roof.



ilssing spark arrestor at the top of the family room chimney.

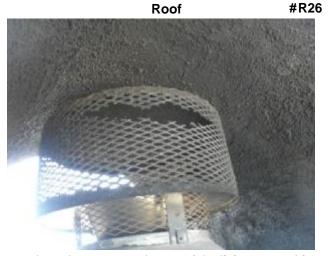

Damaged spark arrestor at the top of the living room chimney.



No cricket flashing installed behind the chimney enclosures.

Exterior

	COMPONENT	CONDITION	ACTION RECOMMENDED	PERSPECTIVE
1	Siding:	Acceptable		
2	Trim/fascias/soffits:	Most Acceptable	Repair - See Comments Below	Moderate Concern
3	Veneer:	Most Acceptable	Repair - See Comments Below	Moderate Concern
4	Doors:	Average	Repair - See Comments Below	Moderate Concern
5	Windows:	Average	Repair - See Comments Below	Moderate Concern
6	Hose faucets:	Acceptable		
7	Electrical cable:	N/A		
8	Exterior electrical:		See the Electrical Page	

			INFORM	ATION	
9	Siding type:	Stucco & Wood	13	Window Type:	Fixed/Sliding
10	Veneer type:	Stone			
11	Trim/fascias type:	Wood	14	Window material:	Aluminum
12	Door type:	Wood, Metal/Glass & Sliders	15	Electric service cable:	Underground

EXTERIOR COMMENTS

- Information Note: There are dual pane windows installed in this home. One of the more common problems associated with this type of window is "fogging" where water is trapped between the two panes of glass. A very diligent inspection is performed from the exterior and interior of the home to detect this problem however, variations in light, time of day, weather and dirt/salt on the windows can mask this problem. In this particular case the windows were very dirty at the time of inspection. For a definite guarantee to detect all failed windows, it is advised that the windows be professionally cleaned and then inspected by a qualified and licensed Glazing Contractor.
 - 1.) The front entry door needs to be refinished. The astragal is damaged and the strike plate is missing for the dead bolt.
 - 2.) The sliding glass door in the master bedroom has some small animal scratches in the glass and the screen door is damaged.
 - 3.) There is moisture damage to the exterior door and both jambs in the west hall bathroom. This door is in need of complete replacement.
 - 4.) There is moisture damage to the base of the double exterior doors in the SW bedroom. Evidence of water intrusion was present on the base boards and walls inside of these doors.
 - 5.) The dual pane glass at the sliding glass door in the family room is fogged.
 - 6.) The exterior door on the west side of the garage has moisture damage to the door and jamb. This door is in need of complete replacement.
 - 7.) There are fogged windows in the following locations: (See above Info Note)
 - A.) The fixed window on the north wall of the dining room.
 - B.) Both windows in the master bathroom.
 - C.) The fixed window in the NE bedroom.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 4 of 22

Exterior

EXTERIOR COMMENTS - Continued

- 16 8.) There are five damaged window screens.
 - 9.) There is a "BB" size hole in the window on the north wall of the garage.
 - 10.) The eaves and fascia boards are in need of painting.
 - 11.) Parts of the stone veneer are missing at the family room chimney enclosure.
 - 12.) Moisture damage was observed in the following locations:
 - A.) The fascia boards at the NE, NW and SW corners of the roof.
 - B.) The fascia board above the water heater closet.
 - C.) The fascia board adjacent to the family room chimney enclosure.
 - D.) Along the entire base of the water heater closet.
 - E.) The wood trim at the front entry stucco arch.
 - F.) The center eave outside of the dining room.
 - 13.) The water heater closet roof is leaking and there are large holes in the drywall inside the closet.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 5 of 22



Moisture damage to the wood trim at the front entry arch.



Moisture damage to the exterior door and jamb at the west hall bathroom.



Moisture damage to the base of the water heater closet.

Exterior

#EX8



Parts of the stone veneer are missing at the family room chimney enclosure.



Moisture damage to the fascia board at the NE corner of the roof.



Damage to the astragal at the front entry door.



Moisture damage to the eave at the north side of the dining room.



Moisture damage to the fascia board at the SW corner of the roof.



Moisture damage to the fascia board above the water heater closet.

Exterior

#EX14



Evidence of water intrusion at the exterior door in the SW bedroom conversion.



Moisture damage to the door and jamb at the exterior door in the SW bedroom.



Moisture damage to the fascia board adjacent to the family room chimney enclosure.

Exterior

#EX24



Parts of the stone veneer are missing at the family room chimney enclosure.

Grounds & Drainage

	COMPONENT	CONDITION	ACTION RECOMMENDED	PERSPECTIVE
1	Drainage:	Acceptable		
2	Trees & shrubs:	Acceptable		
3	Walks & Steps:	Most Acceptable	Repair - See Comments Below	Safety Hazard
4	Porch/Deck:	Acceptable		
5	Driveway:	Most Acceptable	Repair - See Comments Below	Maintenance Item
6	Retaining walls:	Acceptable		
7	Fencing & Gates:	Acceptable	See Comments Below	
8	:			

	INFORMATION						
9	Walks & Steps:	Concrete	13	Porch	Concrete		
10	-	Concrete	14	Location	Front		
11	Location:	Rear	15	Retaining walls:	CMU Block & Stucco		
12	Driveway:	Asphalt & Unpaved	16	:			

GROUNDS & DRAINAGE COMMENTS

17 Soil condition and stability on sloped or steep lots is not determined or within the scope or expertise of this inspection. If concerned, this evaluation would require the expertise of a qualified and licensed Geotechnical Engineer.

General Note: Any reference to grading is limited to only the areas around the foundation or exterior walls. We cannot determine drainage performance of the site or site soil conditions. We do not evaluate any detached structures such as storage sheds and stables, nor mechanically or remotely controlled components such as driveway gates.

Information Note: Fencing on acreage is not inspected.

Information Note: The outbuildings were not included in the scope of this inspection.

Safety Hazard Note: There is no railing at the front entry concrete stairs off the driveway. This can be a falling hazard.

Maintenance Note: The asphalt driveway appears to be in reasonable condition but needs sealant. Cracks and general deterioration were observed.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 8 of 22

Grounds #GD2

Missing railing at the front entry concrete stairs.



General deterioration and cracks in the asphalt driveway.

Heating & Cooling

	COMPONENT	CONDITION	ACTION RECOMMENDED	PERSPECTIVE
	A /Cti	NI/A		
1	A/C operation:			
2	Heating operation:	Functional		
3	System back-up:	N/A		
4	Exhaust system:	N/A		
5	Distribution:	N/A		
6	Thermostat:	Acceptable		
7	Gas Piping:	N/A		
8	Condensate:	N/A		
9	:			
10	Filter:	N/A		

	INFORMATION							
11	# Heating Units:	6	18	# Cooling Units:	0			
12	Heating Types:	Ceiling Electric Resistance	19	A/C Types:				
13	Heating Ages:	<u>38</u> years	20	A/C age:				
14	Heating Fuels:	Electric	21	Filter:	N/A			
15	Distribution:	N/A	22	Heat Source Mfr.	Comfort Zone			
16	Duct Insulation Type:	N/A	23	A/C Source Mfr.				
17	Gas Shutoff Location:	N/A - Property is all Electric						

HEATING & COOLING COMMENTS

Our inspection of the HVAC systems is limited to the normal functions of the systems. Independent evaluations including adequacy/inadequacy of heating and cooling systems (such as cracked heat exchangers, air conditioning pressure tests coolant charge, line integrity, air balance or evaporative cooling coils, etc.) are not within the scope of this inspection. Thermostats are not checked for calibration or timer functions. Normal service maintenance of these systems is recommended to be performed annually.

Information Note: There are five radiant heating systems and one base board heater in this home. These were tested and found to be operable at the time of inspection.

- 1.) There is no heat provided to the NW bedroom conversion.
- 2.) The control knob is missing for the base board heater in the SW bedroom conversion.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 10 of 22

Plumbing

	COMPONENT	CONDITION	ACTION RECOMMENDED	PERSPECTIVE
1	Supply pipes:	Most Acceptable	Repair - See Comments Below	Moderate Concern
2	Waste/vent pipes:	Acceptable		
3	Funct'l water flow:	Acceptable		
4	Funct'l waste drain:	Most Acceptable	Recommend further Evaluation by a Plumbing Contractor	Active Leak
5	Well system:	Not Inspected	See Comment Below	
6	Septic system:	Not Inspected	See Comment Below	
7	Water heater:	Most Acceptable	Repair - See Comments Below	Safety Hazard
8	TPR Valve:	Most Acceptable	Repair - See Comments Below	Safety Hazard
			INFORMATION	
9	Water supp	Private well & M	unicipal 14 Waste system Private Septic Syst	em

represented as: represented as: 15 Septic location: South Yard 10 Supply pipes: Copper Waste/Vent pipes: ABS Plastic Pipe insulation type: None 17 Water Heater Mfr.: Rheem Water Shutoff Location: West Wall 12 18 Water Heater Gallons: 50 Age: 2 years 13 Well location: N/A 19 Water Heater Fuel: Electric

PLUMBING COMMENTS

20 The water temperature is not tested or verified. Water that is hotter than the manufacturers recommended setting on the water heater is not advised and can be a scalding hazard. We recommend that the temperature setting on the hot water heater be checked at move-in for safety.

Shut off valves and angle stops at kitchen or bathroom sinks and toilets are not tested due to the possibility of leaking.

Information Note: The water pressure was measured at 40 psi. This is within a normal and acceptable range.

Information Note: There is a septic system installed at the property. Evaluation of the septic system is beyond the scope of this inspection. Recommend evaluation by a qualified and licensed Septic Company prior to close of escrow.

Information Note: There is a well system at the property. Evaluation of the well system and the associated plumbing & electrical systems is beyond the scope of this inspection. Recommend evaluation by a qualified and licensed Well Company prior to close of escrow.

Information Note: It appears that the potable water supplied to the home is a municipal system however; this should be verified with the owner.

Safety Hazard Note: The water heater is inadequately braced. A second strap is required.

Safety Requirement: Blocking is needed between the water heater and the adjacent wall to prevent it from rocking in the event of an earthquake. This is required as part of properly installing the earthquake straps.

Safety Hazard Note: The discharge pipe for the TPR valve on the water heater terminates improperly. It is required for this pipe to terminate at the exterior of the closet.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 11 of 22

Plumbing

PLUMBING COMMENTS - Continued

- 20 1.) There is excessive corrosion at the water heater shut off valve and the water lines above the water heater.
 - 2.) The reserve tank for the solar hot water assist system is 27 years old with rust damage to the base of the tank. This tank is beyond a normal life expectancy and will need to be replaced soon.
 - 3.) The vent pipe at the exterior south wall of the kitchen terminates improperly. This pipe should terminate above the roof.
 - 4.) Moisture probe testing at the water stain on the base board in the master bedroom indicates an active concealed plumbing leak in the hall bathroom vanity which is directly behind this location. Recommend further evaluation by removing the drywall to determine the cause of this leak and determine if there is any moisture related damage prior to close of escrow.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 12 of 22



The solar hot water reserve tank is old and beyond a normal life expectancy.



Corroded valve at the water heater.



Corroded water line above the water heater.



Improperly terminated vent pipe at the exterior north wall of the kitchen.



Concealed plumbing leak behind the vanity in the east hall bathroom.

Electrical System

	COMPONENT CONDITION		ACTION RECOMMENDED	PERSPECTIVE
1	Wiring at main box:	Most Acceptable	Fire Hazard - Advise repairs by an Electrical Contractor	Fire Safety Hazard
2	Ground:	Acceptable		
3	GFCI:	Most Acceptable	Repair - See Comments Below	Safety Upgrade
4	Amperage:	Acceptable		
5	Wiring:	Most Acceptable	Safety Hazard - Advise repairs by an Electrical Contractor	Safety Hazard
6	Outlets:	Most Acceptable	Repair - See Comments Below	Maintenance Item
7	Lighting:	Most Acceptable	Safety Hazard - Advise repairs by an Electrical Contractor	Safety Hazard
8	:			
				-

			INFO	RMATION	
9	Amps:	200	14	Branch circuit wiring:	Copper
10	Volts:	110/220	15	Grounding:	Water Pipes
11	Main box location:	SW Wall	16	Ground fault protection at:	Exterior & Bathrooms
12	Main Disconnect:	At Main Panel			
13	Main service	Copper	17	Main box type:	Breakers
	conductor.	оорро.	18	Wiring type:	Romex

ELECTRICAL SYSTEM COMMENTS

19 Information Note: There is furniture and storage throughout the home and detached garage which may conceal faulty wiring and restricts the ability to test all of the outlets.

Maintenance Note: The circuit breakers in the main electrical panel and garage subpanel are not labeled.

Fire Safety Hazard Note: There is double tapping in the main electrical panel. (This is where two conductors are connected to a single circuit breaker.) This is advised to be corrected by a qualified and licensed Electrical Contractor.

Safety Hazard Note: The coupler is missing at the 30 amp 220 volt circuit breakers in the main electrical panel.

Safety Hazard Note: The electrical subpanel in the garage is improperly wired. The neutral conductors should be isolated from the grounding conductors. This is advised to be corrected by a qualified and licensed Electrical Contractor.

Fire Safety Hazard Note: There is overfusing in the electrical subpanel in the garage. (This is where the amperage rating of the circuit breaker is greater than the conductor connected to it.) This is advised to be corrected by a qualified and licensed Electrical Contractor.

Safety Upgrade Note: The electrical subpanel in the detached garage has no separate source of grounding.

Safety Upgrade Note: There is no GFCI protection for the outlets in the garage or kitchen due to the age of this home. Recommend upgrading for safety.

1.) Outdoor rated junction boxes and cover plates are needed at the outlet and light switch on the backyard patio cover post.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 13 of 22

Electrical System

ELECTRICAL SYSTEM COMMENTS - Continued

19 2.) There is a broken light fixture that has been wired with a temporary chord on the exterior SW
eave of the garage. This light is recommended to be removed.

Safety Hazard Note: Most of the ceiling florescent lights in the garage are inoperable with exposed live wiring.

3.) The cover plate	is broken	at the light	switch in t	the garage
---------------------	-----------	--------------	-------------	------------

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 14 of 22

Electrical #EL21

Damaged light fixture at the exterior SW corner of the garage.



Damaged ceiling light fixtures in the garage.

	Ter	ry Home Inspection	Services, Inc. PO Box 2705 Atascadero, CA 93423 (805) 434-2	694
			Kitchen & Laundry	
	COMPONENT	CONDITION	ACTION RECOMMENDED	PERSPECTIVE
	KITCHEN			
1	Walls/ceiling/floor:		See the Interior Page	
2	Doors & windows:	Acceptable		
3	Heating & cooling:		See the HVAC Page	
4		Most Acceptable	Repair - See Comments Below	Maintenance Item
5	Sink plumbing:	Acceptable		
	APPLIANCES			
6	Disposal:	Functional		
7	Dishwasher:	Functional		
8	:			
9	Exhaust fan:			
10 11	Microwave:	Functional		
12				
13	Range/oven:	Functional		
14	Gas or electric?			
			_	
15	LAUNDRY		See the Interior Page	
16	Walls/ceiling/floor: Doors & windows:		See the Interior Page	
17	Washer plumbing:	Acceptable		
18	Sink plumbing:			
19	Cabinets/shelves:			
20	Heating & cooling:		See the HVAC Page	
21		Most Acceptable	Repair - See Comments Below	Maintenance Item
22	:			
23	:			
24	Drver service:			
25	Gas or electric?	Electric		
			KITCHEN AND LAUNDRY COMMENTS	
26	systems. These it as calibration of t are outside the so interiors and show Dishwasher clean	ems are tested un- imers, clocks, hea cope of this inspec- uld be checked du ling and drying ad	nts is limited to the built in appliances and plumbing der normal operating conditions. Extensive evaluation such t settings, thermostat accuracy, self-cleaning functions, etc. tion. Stored personal items can restrict viewing of cabinet ring your final walkthrough prior to close of escrow. equacy is not verified. uct safety alerts are added almost daily. If client(s) is/are	

Product recalls and consumer product safety alerts are added almost daily. If client(s) is/are concerned about appliances or other items in the home that may be on such lists, client(s) may wish to visit the U.S. Consumer Product Safety Commission (CPSC)web site at www.cpsc.gov or www.cpsc.gov</a

- 1.) The base of the cabinet below the kitchen sink is missing.
- 2.) The dryer lint exhaust vent hood is missing.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 15 of 22

Bathrooms

	COMPONENT	CONDITION	ACTION RECOMMENDED	PERSPECTIVE
1	Walls, ceiling, floor:		See the Interior Page	
2	Doors & windows:		See the Interior Page	
3	Heating & cooling:		See the HVAC Page	
4	Cabinets & counter:	Acceptable		
5	Vents:	Acceptable		
6	Sinks:	Acceptable		
7	Toilets:	Acceptable		
8	Tubs:	Acceptable		
9	Showers:	Most Acceptable	Repair - See Comments Below	Moderate Concern
10	:			
	•			

BATHROOMS INSPECTED

11 # of Half baths: 12 # of Full baths: 2 13 # of 3/4 baths: 1

BATHROOM COMMENTS

Our inspection of the bathrooms is to report on visible leaks and operations of the fixtures. Inaccessible piping and shower pans are outside the scope of this inspection. Shower pans, enclosures and doors are not tested for water tightness, visual observations only. All areas under sinks may not be visible due to stored items and should be checked during your final walkthrough prior to close of escrow.

Information Note: The bathroom toilets are low flow 1.6 GPF.

Information Note: The shower heads are low flow 2.5 GPM or less at the master bathroom and center hall bathroom. The shower in the west hall bathroom is not a low flow type.

Information Note: There are low flow aerators on the bathroom sink faucets.

Maintenance Note: There is a faulty diverter valve at the tub/shower in the master bathroom. This allows water to partially flow out the tub spout when the shower is operated.

Information Note: The shower wall tiles have been installed with mastic glue to the drywall in the east hall bathroom. This is considered a substandard installation by most tradesman. The tiles may be subject to future delamination.

- 1.) The diverter valve at the tub/shower in the east hall bathroom is defective and stuck in shower mode.
- 2.) The sink drain stoppers are missing in both of the hall bathrooms.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 16 of 22

meet the National Fire Protection Agency (NFPA) current standards.

Safety Upgrade Note: Recommend installing smoke detectors in each of the remaining four bedrooms.

Safety Hazard Note: There is no carbon monoxide detector installed in the home as required.

- 1.) There are several cracked floor tiles in the master and east hall bathrooms.
- 2.) The closet door guides are missing in the SW bedroom and center hall bedroom.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 17 of 22

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Copyright © 2017 New Image Software, Inc.™ All rights reserved. Rev 12/2015

Page 18 of 22

Interior Rooms

#IR30



Damaged refractory plate in the living room fireplace.

Garage & Carport

	COMPONENT	CONDITION	ACTION RECOMMENDED	PERSPECTIVE
			T	T
1	Roof:	Average	See Comments Below	
2	Walls:	Acceptable		
3	Eaves:	Acceptable		
4	Electrical:		See the Electrical Page	
5	Gutters:		See the Roof Page	
	INTERIOR			
6	Walls/ceiling/floor:	Most Acceptable	Repair - See Comments Below	Moderate Concern
7	Firewall/firedoor:	N/A		
8	Doors & windows:	Acceptable		
9	Garage doors:	Acceptable		
10	Door openers:	Most Acceptable	Repair - See Comments Below	Safety Hazard
11	Electrical:		See the Electrical Page	
12	Heating & cooling:	N/A		

		INI	FORMATION		
	EXTERIOR			INTERIOR	
13	Location:	Detached -separate building	17	Walls & ceilings:	Sheet Rock & Partly Unfinished
14	Roof covering:	Fiberglass Shingle	18	Floors:	Concrete
15	Roof age:	25 Years old (Estimate)	19	Garage door:	Double Overhead
16	Gutters:	None			

GARAGE & CARPORT COMMENTS

- Information Note: The garage is approximately 50% blocked by the occupants storage. Check this area carefully during the final walkthrough when the garage is vacant. Any concerns should be reinspected prior to close of escrow.
 - 1.) The garage roof shingles are older with general deterioration and delamination of the aggregate coating on the shingles. This roof is near the end of a normal life expectancy.
 - 2.) The drywall is damaged in places at the interior of the garage.

Safety Hazard Note: The pressure switch safety reverse at the garage vehicle door opener is defective. Recommend corrective repairs by a licensed Garage Door Contractor.

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 19 of 22

#GC20 Garage Garage



Damaged drywall at the interior SE wall of the garage.



General deterioration of the garage roof shingles.

1 Access: Acceptable 2 Framing: Acceptable 3 Sheathing: Acceptable 4 Insulation: Acceptable								
COMPONENT CONDITION ACTION RECOMMENDED PERSPECTIV 1		Tei	ry Home Inspection	Services, Inc. PO Box 270)5 Atasc	adero, CA 93423	(805) 434-269	4
1 Access: Acceptable 2 Framing: Acceptable 3 Sheathing: Acceptable 4 Insulation: Most Acceptable 5 Ventilation: Most Acceptable Repair - See Comments Below Maintenance Its 6 Exposed wiring: See the Electrical Page 7 Plumbing vents: Acceptable 8 Chimney & flues: Acceptable 9 Vapor Retarder: N/A 10				Att	ic			
2 Framing: Acceptable 3 Sheathing: Acceptable 4 Insulation: Acceptable 5 Ventilation: Most Acceptable Repair - See Comments Below Maintenance Interpretation: Most Acceptable Repair - See Comments Below Maintenance Interpretation: See the Electrical Page 7 Plumbing vents: Acceptable Chimney & flues: Acceptable N/A Interpretation: Most Acceptable N/A Interpretation: N/A Interpretation: Interpretation: Master Closet & Pantry Interpretation: Master Closet & Pantry Interpretation: Batts 4" Access locations: Master Closet & Pantry Interpretation: Batts 4" ATTIC COMMENTS 17 Information Note: Some areas of the attic can be limited due to low clearances, ducting and insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. 1.) The screen mesh is damaged at the attic ventilation opening at the SE eave.		COMPONENT	CONDITION	ACTI	ON REC	OMMENDED		PERSPECTIVE
3 Sheathing: Acceptable Insulation: Acceptable Repair - See Comments Below Maintenance Its Exposed wiring: See the Electrical Page 7 Plumbing vents: Acceptable Chimney & flues: Acceptable Vapor Retarder: N/A Insulation: Master Closet & Pantry Is Sheathing: Plywood 11 # of Attic areas: Insulation: Master Closet & Pantry Is Sheathing: Plywood 12 Access locations: Master Closet & Pantry Is Sheathing: Plywood 13 Access by: Hatch Is Insulation: Batts 4" ATTIC COMMENTS 17 Information Note: Some areas of the attic can be limited due to low clearances, ducting and insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If Client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. 1.) The screen mesh is damaged at the attic ventilation opening at the SE eave.	1	Access:	Acceptable					
4 Insulation: Acceptable Ventilation: Most Acceptable Repair - See Comments Below Maintenance Its Exposed wiring: See the Electrical Page 7 Plumbing vents: Acceptable Chimney & flues: Acceptable Vapor Retarder: N/A Insulation: INFORMATION 11 # of Attic areas: 2	2	Framing:	Acceptable					
See the Electrical Page Plumbing vents: Acceptable Chimney & flues: Acceptable Vapor Retarder: N/A Hof Attic areas: 2	3	Sheathing:	Acceptable					
6 Exposed wiring: 7 Plumbing vents: 8 Chimney & flues: 9 Vapor Retarder: 10 INFORMATION 11 # of Attic areas: 2 14 Framing: Conventional 12 Access locations: Master Closet & Pantry 15 Sheathing: Plywood 13 Access by: Hatch 16 Insulation: Batts 4" ATTIC COMMENTS 17 Information Note: Some areas of the attic can be limited due to low clearances, ducting and insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. 1.) The screen mesh is damaged at the attic ventilation opening at the SE eave.	4	Insulation:	Acceptable					
7 Plumbing vents: Acceptable 8 Chimney & flues: Acceptable 9 Vapor Retarder: N/A 10 INFORMATION	5	Ventilation:	Most Acceptable	Repair - See Comments B	elow			Maintenance Item
8 Chimney & flues: Acceptable 9 Vapor Retarder: N/A 10 INFORMATION IN	6	Exposed wiring:		See the Electrical Page				
9 Vapor Retarder: N/A INFORMATION INFORMATION 11 # of Attic areas: 2 14 Framing: Conventional 12 Access locations: Master Closet & Pantry 15 Sheathing: Plywood 13 Access by: Hatch 16 Insulation: Batts 4" ATTIC COMMENTS 17 Information Note: Some areas of the attic can be limited due to low clearances, ducting and insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. 1.) The screen mesh is damaged at the attic ventilation opening at the SE eave.	7	Plumbing vents:	Acceptable					
INFORMATION 11 # of Attic areas: 2	8	Chimney & flues:	Acceptable				, and the second	
INFORMATION 11 # of Attic areas: 2	9	Vapor Retarder:	N/A					
11 # of Attic areas: 2	10	:						
11 # of Attic areas: 2				INFORMA	TION			
Access locations: Master Closet & Pantry 15 Sheathing: Plywood Access by: Hatch ATTIC COMMENTS ATTIC COMMENTS 17 Information Note: Some areas of the attic can be limited due to low clearances, ducting and insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. 1.) The screen mesh is damaged at the attic ventilation opening at the SE eave.								
ATTIC COMMENTS 17 Information Note: Some areas of the attic can be limited due to low clearances, ducting and insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. 1.) The screen mesh is damaged at the attic ventilation opening at the SE eave.	11	# of Attic areas	: 2		14	Framing:	Conventional	
Information Note: Some areas of the attic can be limited due to low clearances, ducting and insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. 1.) The screen mesh is damaged at the attic ventilation opening at the SE eave.	12	Access locations	: Master Closet &	Pantry	15	Sheathing:	Plywood	
 Information Note: Some areas of the attic can be limited due to low clearances, ducting and insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. The screen mesh is damaged at the attic ventilation opening at the SE eave. 	13	Access by	: Hatch		16	Insulation:	Batts 4"	
Insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. 1.) The screen mesh is damaged at the attic ventilation opening at the SE eave.				ATTIC COMM	MENTS			
	17	 Information Note: Some areas of the attic can be limited due to low clearances, ducting and insulation. The presence of environmental hazards, materials or conditions including, but not limited to lead, asbestos, radon, toxic, combustible or corrosive contaminants is outside the scope of this inspection. If client(s) is/are are concerned regarding these matters, it is recommended to obtain the consultation services of an appropriate and qualified expert prior to close of escrow. The screen mesh is damaged at the attic ventilation opening at the SE eave. 						

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 21 of 22

	Tei	rry Home Inspection	Services, Inc. PO Box 2709	5 Ataso	adero, CA 93423 (805) 434-2	2694	
			Founda	atic	n		
	COMPONENT	CONDITION			OMMENDED	PERSPECTIVE	
	Foundation Type	Slab					
1	Access:						
2	Foundation walls:	i a					
3	Floor framing:	i					
4	Insulation:						
5	Ventilation:						
6	Sump pump:	N/A					
7	Dryness/drainage:	N/A					
8	Floor/Slab:	Acceptable	See Comments Below				
9	Vapor Retarder:	ļ—————————————————————————————————————					
0	Anchor Bolts:		Not Visible				
			INFORMAT	ION			
					_		
11	Foundation walls:			14	Beams:		
2	Floors:			15	Piers:		
3	Joist/Truss Detail:			16	Sub Floor:		
				17	Insulation:		
			FOUNDATION CO	ОММЕ	NTS		
18	Engineering analysis of a building structure can only be performed by a licensed Structural Engineer using measurements, calculations and other scientific means of evaluation. Engineering is beyond the scope of this inspection. General Note: All concrete floor slabs experience some degree of cracking due to shrinkage during the curing process. In most instances floor coverings prevent the recognition of cracks and settlement in all but the most severe cases. Where carpeting or floor finishes are installed, the materials and condition of the slab underneath cannot be determined. Areas hidden from view by finished walls or stored items cannot be evaluated and are outside the scope of this visual inspection. We are not specialists, and in the absence of any major defects, we may not recommend that you consult with a foundation contractor, a structural engineer or a geologist. This should not deter you from seeking the opinion of any such expert. It is always recommended that inquiry be made with the seller about the knowledge of any prior foundation or structural repairs. Information Note: The concrete slab on grade is not visible due to the finish flooring in the home. There were no secondary visible observations or problems throughout the accessible portions of the home which would indicate a structural deficiency with the slab.						

1511 Dale Avenue, Arroyo Grande, CA 93420-Antonio R & Ida Martinez Revocable Living Trust

Page 22 of 22

Contact: Phone:

Location: 1511 Dale Avenue

Arroyo Grande, CA 93420

This summary is not the entire report. The full report may include additional information of interest or concern to the client. It is strongly recommended that the client promptly read the complete report.

2 - Roof

Maintenance Note: Recommend installing gutters and down spouts to improve lot drainage. The down spouts should be extended to drain the surface water away from the perimeter of the foundation.

- 1.) There are no cricket flashing behind the chimney enclosures. This is required when the chimney enclosure is greater than 30 inches in width to divert water around the chimney. This may render these areas to potential leaks.
- 2.) Field shingles have been used for caps at the ridge line on the roof. This is an unconventional installation and may subject the ridge shingles to future wind damage particularly as the roof gets older.

Fire Safety Hazard Note: The spark arrestor is missing at the top of the family room fireplace and the spark arrestor is damaged at the top of the living room fireplace.

- 3 Exterior
- 1.) The front entry door needs to be refinished. The astragal is damaged and the strike plate is missing for the dead bolt.
- 2.) The sliding glass door in the master bedroom has some small animal scratches in the glass and the screen door is damaged.
- 3.) There is moisture damage to the exterior door and both jambs in the west hall bathroom. This door is in need of complete replacement.
- 4.) There is moisture damage to the base of the double exterior doors in the SW bedroom. Evidence of water intrusion was present on the base boards and walls inside of these doors.
- The dual pane glass at the sliding glass door in the family room is fogged.
- 6.) The exterior door on the west side of the garage has moisture damage to the door and jamb. This door is in need of complete replacement.
- 7.) There are fogged windows in the following locations: (See above Info Note)
 - A.) The fixed window on the north wall of the dining room.
 - B.) Both windows in the master bathroom.
 - C.) The fixed window in the NE bedroom.
- 4 Exterior
- 8.) There are five damaged window screens.
- 9.) There is a "BB" size hole in the window on the north wall of the garage.
- 10.) The eaves and fascia boards are in need of painting.
- 11.) Parts of the stone veneer are missing at the family room chimney enclosure.
- 12.) Moisture damage was observed in the following locations:
 - A.) The fascia boards at the NE, NW and SW corners of the roof.
 - B.) The fascia board above the water heater closet.
 - C.) The fascia board adjacent to the family room chimney enclosure.
 - D.) Along the entire base of the water heater closet.
 - E.) The wood trim at the front entry stucco arch.
 - F.) The center eave outside of the dining room.
- 13.) The water heater closet roof is leaking and there are large holes in the drywall inside the closet.

The report is provided as a courtesy for quicker access to DEFICIENCIES within the inspection report. This is not intended as a substitute for reading the inspection report. Items listed may be discussed further on the corresponding report page. There also may be findings other than what is listed on this page.

Contact: Phone:

Location: 1511 Dale Avenue

Arroyo Grande, CA 93420

5 - Grounds

Safety Hazard Note: There is no railing at the front entry concrete stairs off the driveway. This can be a falling hazard.

Maintenance Note: The asphalt driveway appears to be in reasonable condition but needs sealant. Cracks and general deterioration were observed.

6 - HVAC

- 1.) There is no heat provided to the NW bedroom conversion.
- 2.) The control knob is missing for the base board heater in the SW bedroom conversion.

7 - Plumbing

Information Note: There is a septic system installed at the property. Evaluation of the septic system is beyond the scope of this inspection. Recommend evaluation by a qualified and licensed Septic Company prior to close of escrow.

Information Note: There is a well system at the property. Evaluation of the well system and the associated plumbing & electrical systems is beyond the scope of this inspection. Recommend evaluation by a qualified and licensed Well Company prior to close of escrow.

Information Note: It appears that the potable water supplied to the home is a municipal system however; this should be verified with the owner.

Safety Hazard Note: The water heater is inadequately braced. A second strap is required.

Safety Requirement: Blocking is needed between the water heater and the adjacent wall to prevent it from rocking in the event of an earthquake. This is required as part of properly installing the earthquake straps.

Safety Hazard Note: The discharge pipe for the TPR valve on the water heater terminates improperly. It is required for this pipe to terminate at the exterior of the closet.

8 - Plumbing

- 1.) There is excessive corrosion at the water heater shut off valve and the water lines above the water heater.
- 2.) The reserve tank for the solar hot water assist system is 27 years old with rust damage to the base of the tank. This tank is beyond a normal life expectancy and will need to be replaced soon.
- 3.) The vent pipe at the exterior south wall of the kitchen terminates improperly. This pipe should terminate above the roof.
- 4.) Moisture probe testing at the water stain on the base board in the master bedroom indicates an active concealed plumbing leak in the hall bathroom vanity which is directly behind this location. Recommend further evaluation by removing the drywall to determine the cause of this leak and determine if there is any moisture related damage prior to close of escrow.

9 - Electrical

Maintenance Note: The circuit breakers in the main electrical panel and garage subpanel are not labeled.

Fire Safety Hazard Note: There is double tapping in the main electrical panel. (This is where two conductors are connected to a single circuit breaker.) This is advised to be corrected by a qualified and licensed Electrical Contractor.

Safety Hazard Note: The coupler is missing at the 30 amp 220 volt circuit breakers in the main electrical panel.

Safety Hazard Note: The electrical subpanel in the garage is improperly wired. The neutral conductors should be isolated from the grounding conductors. This is advised to be corrected by a qualified and licensed Electrical Contractor.

The report is provided as a courtesy for quicker access to DEFICIENCIES within the inspection report. This is not intended as a substitute for reading the inspection report. Items listed may be discussed further on the corresponding report page. There also may be findings other than what is listed on this page.

Contact: Phone:

Location: 1511 Dale Avenue

Arroyo Grande, CA 93420

Fire Safety Hazard Note: There is overfusing in the electrical subpanel in the garage. (This is where the amperage rating of the circuit breaker is greater than the conductor connected to it.) This is advised to be corrected by a qualified and licensed Electrical Contractor.

Safety Upgrade Note: The electrical subpanel in the detached garage has no separate source of grounding.

Safety Upgrade Note: There is no GFCI protection for the outlets in the garage or kitchen due to the age of this home. Recommend upgrading for safety.

1.) Outdoor rated junction boxes and cover plates are needed at the outlet and light switch on the backyard patio cover post.

10 - Electrical

2.) There is a broken light fixture that has been wired with a temporary chord on the exterior SW eave of the garage. This light is recommended to be removed.

Safety Hazard Note: Most of the ceiling florescent lights in the garage are inoperable with exposed live wiring.

- 3.) The cover plate is broken at the light switch in the garage.
- 11 Kitchen & Laundry
- 1.) The base of the cabinet below the kitchen sink is missing.
- 2.) The dryer lint exhaust vent hood is missing.

12 - Bathroom

Maintenance Note: There is a faulty diverter valve at the tub/shower in the master bathroom. This allows water to partially flow out the tub spout when the shower is operated.

Information Note: The shower wall tiles have been installed with mastic glue to the drywall in the east hall bathroom. This is considered a substandard installation by most tradesman. The tiles may be subject to future delamination.

- 1.) The diverter valve at the tub/shower in the east hall bathroom is defective and stuck in shower mode.
- 2.) The sink drain stoppers are missing in both of the hall bathrooms.

13 - Interior Rooms

Fire Safety Hazard Note: The smoke detectors in the west hall and SW bedroom are inoperable.

Safety Recommendation: The smoke detectors are tested at the time of inspection however, this only determines that they are functional on the day of the inspection. Smoke detectors can fail at any time. Retest all the smoke detectors during the final walkthrough and again upon moving in. We recommend installing new batteries in all of the smoke detectors upon moving in and testing weekly as recommended by the Consumer Product Safety Commission. Also, any older ionization type smoke detectors should be replaced with new ones that are photoelectric and meet the National Fire Protection Agency (NFPA) current standards.

Safety Upgrade Note: Recommend installing smoke detectors in each of the remaining four bedrooms.

Safety Hazard Note: There is no carbon monoxide detector installed in the home as required.

- 1.) There are several cracked floor tiles in the master and east hall bathrooms.
- 2.) The closet door guides are missing in the SW bedroom and center hall bedroom.
- 14 Interior Rooms
- 3.) The carpeting is in poor condition at the SW and NW bedrooms.

The report is provided as a courtesy for quicker access to DEFICIENCIES within the inspection report. This is not intended as a substitute for reading the inspection report. Items listed may be discussed further on the corresponding report page. There also may be findings other than what is listed on this page.

Contact: Phone:

Location: 1511 Dale Avenue

Arroyo Grande, CA 93420

Fire Safety Hazard Note: The refractory plates are damaged in the living room fireplace and the metal plates are rusted and pitted in the family room fireplace. These fireplaces may be unsafe to use. Recommend further evaluation of this condition by a certified and licensed Fireplace Contractor prior to close of escrow.

15 - Garage

- 1.) The garage roof shingles are older with general deterioration and delamination of the aggregate coating on the shingles. This roof is near the end of a normal life expectancy.
- 2.) The drywall is damaged in places at the interior of the garage.

Safety Hazard Note: The pressure switch safety reverse at the garage vehicle door opener is defective. Recommend corrective repairs by a licensed Garage Door Contractor.

16 - Attic

1.) The screen mesh is damaged at the attic ventilation opening at the SE eave.

Information Note: There is no access to the attic space above the finished room in the garage.
