



NEWDOC

DEH APN FILE TARGET SHEET
ARCHIVE RECORD
Pre-KIVA & Existing APN Records

Document Name: LARC _____
(LARC_KIVA Per Num_APN)

Document Type: Legacy Septic System Documents

APN(s) 121-330-05

Number of Pages: 6

Document Prepared by: EK

Document Preparation Date: 4-16-09

Office Source: San Marcos

5801

APPLICATION AND PERMIT FOR SEPTIC TANK

EXPIRES ONE YEAR FROM APPLICATION DATE

PERMIT ISSUED

DATE

NUMBER

T 61755

BY:

Jr

6-13-84

~~B-13300~~

NAME OF OWNER

OWNER'S MAILING ADDRESS

PHONE

WILLIAMS, TERRY

c/o Robert Lackey, P.O. Box 280 Fallbrook

ADDRESS OR LOCATION OF JOB

5088 off San Jacinto Circle, Fallbrook

C.T. 186.05

ASSESSOR'S PARCEL NUMBER

SEPTIC TANK CONTRACTOR

PHONE

121-330-05

Lenfers 13/84 2231533 997 0061755 A

50.00 CHECK

SPACE BELOW FOR DEPARTMENTAL USE ONLY

50.00

PERMANENT ☒

TEMPORARY ☐

LAYOUT APPROVAL:

PERCOLATION TEST Terry Williams 10/81

SEEPAGE PIT (DEPTH)

SUBDIVISION

SEPTIC TANK 1000 gal

Fennell

C/C-B/A P/M Pcl C

TILE LINE 460' + 100% reserve

SANITARIAN
5-18-84

FIELD APPROVAL

REMARKS see notes on layout

DATE

REPAIR ☐

REMARKS

WATER SOURCE: FPUD

TYPE OF STRUCTURE: COMMERCIAL ☐ RESIDENTIAL 3 BR

DATE REQUESTED

DATE INSPECTED

APPROVED

DISAPPROVED

REINSPECTION NUMBER

DATE REINSPECTED

SANITARIAN'S APPROVAL

6-13-84

6/14/84

Fennell

DHSISAN LU-1 (2/82)

SAN DIEGO CO. DEPARTMENT OF HEALTH SERVICES
1700 PACIFIC HWY., SAN DIEGO, CALIF. 92101

SANITARIAN

☐ I hereby certify that I am the owner of the property for which I am applying for a permit to construct a subsurface sewage disposal system. I do not intend to sell or offer for sale this property within one year after completion of construction. I therefore request an exemption from the requirement that I have a proper contractor's license for such construction.

☐ I hereby certify that I am a contractor licensed in the State of California, to perform the specific tasks for which I am presently applying. My license is in full force and effect, and will remain so to the best of my knowledge throughout the duration of this project. My contractor's license is, as follows:

1. In the name of _____
2. State License No. _____
3. Classification: _____
(Class A or C42 required per Business & Professional Code, Chapter 9, Sec. 7056, and Calif. Administrative Code, Chapter 8 T - 16, Sec. 754.4)

I am informed and understand that any false information could result in a penalty of not more than \$500 for each violation, as provided in Business and Professional Code, Sec. 7031.5.

Signed: _____

FOR OWNER

Date _____

6-13-84

COUNTY OF SAN DIEGO DEPARTMENT OF PUBLIC HEALTH

SEPTIC TANK INSTALLATION REPORT

SOIL CONDITIONS OF TRENCH OR SEEPAGE PIT

PERCOLATION TEST

E06-70083-13

DEPARTMENT USE ONLY

Issue permit ☒ Yes ☐ No
 Final parcel map required: ☐ Yes ☒ No
 Sanitarian: JOHN CASTON
 Date: 09.22.1981

NOTE Layout

Date July 9, 1981 12-21-82OWNER'S NAME TERRY WILLIAMSADDRESS 476 W. Vermont, #102

CONTRACTOR _____

ADDRESS _____

Legal Location APN 121-22, Portion of 34

Lot (Parcel "C") _____

Block _____

Test Location Off San Jacinto Circle, Sleeping Indian area

(NUMBER, STREET AND TOWN)

THIS REPORT WILL NOT BE REVIEWED UNTIL THE FOLLOWING INFORMATION IS ATTACHED:

1. Lot Location (locate by street)
2. Existing and Proposed Structures
3. Surfaced Areas
4. Lot Grade
5. Wells
6. Utility Water Lines
7. Test Holes
8. Sub-Surface Disposal System
9. Cuts and-Fill
10. All calculations on 8 1/2 x 11" Sheet

SUB-SURFACE DRAINAGE

PERCOLATION TEST	TEST	DEPTH OF HOLE	TIME FOR H ₂ O	SAFETY FACTOR	TIME/INCH	AVE. TIME/IN
Last two readings shall not vary more than 10%	1.					39
	2.	SEE ATTACHED SHEET				
	3.					
	4.					

LEACHING SEEPAGE PITS - Provide soils log and calculations on 8 1/2 x 11" sheet

DEPTH	COARSE SAND OR GRAVEL	FINE SAND	SANDY LOAM OR SANDY CLAY	CLAY WITH CONSIDERABLE SAND OR GRAVEL	EFFECTIVE ABSORP. AREA

TYPE OF SOIL: Give specific information (clay-adobe-decomposed granite, etc.)

Surface: Brownish, silty loam with clay1 ft. below surface: "2 ft. below surface: "3 ft. below surface: "

5 17

8 to 10 ft. below surface Light, tan, silty decomposed granite with trace claySource of water Fallbrook Public Utility Depth of water table 17 feet plusProposed structure: No. One Type ResidenceNo. of bedrooms: Three , and/or maximum capacity: _____

RECOMMENDATIONS:

Size tank 1,000 gal.
 Drainage tile 460 ft.
 Trench width 1.5 ft.
 Trench depth 5.0 ft.
 Seepage pit width _____ ft.
 Seepage pit depth _____ ft.

I have reviewed this percolation data and design of the subsurface sewage disposal system for this parcel and find the data and design to be accurate and in compliance with the State and local regulations and good engineering practices

REGISTERED ENGINEER

476 W. Vermont

Address

743-1214


Phone

25115

(REG. NO.)

7/9/81

Date



Williams, Terry


"I CERTIFY THAT THE LAYOUT DRAWING SHOWS THE LOCATION OF ALL PUBLIC WATER LINES ON THE LOT AND ALL PUBLIC WATER LINES THAT ARE WITHIN 20 FEET OF THE LOT BOUNDARIES."

LEGEND


- 460' ○ PERC TEST
- 460' — LEACH LINE
- 460' - - - 100% RESERVE
- - 15' + PROFILE HOLE
- HOUSE TO HAVE RAISED WOOD FLOORS.

NOTE: A SEPTIC TANK PERMIT MUST BE OBTAINED WITHIN 30 DAYS OR THIS APPROVAL WILL BE SUBJECT TO FIELD RECHECK AND A NEW FEE.

SCALE 1"=100'

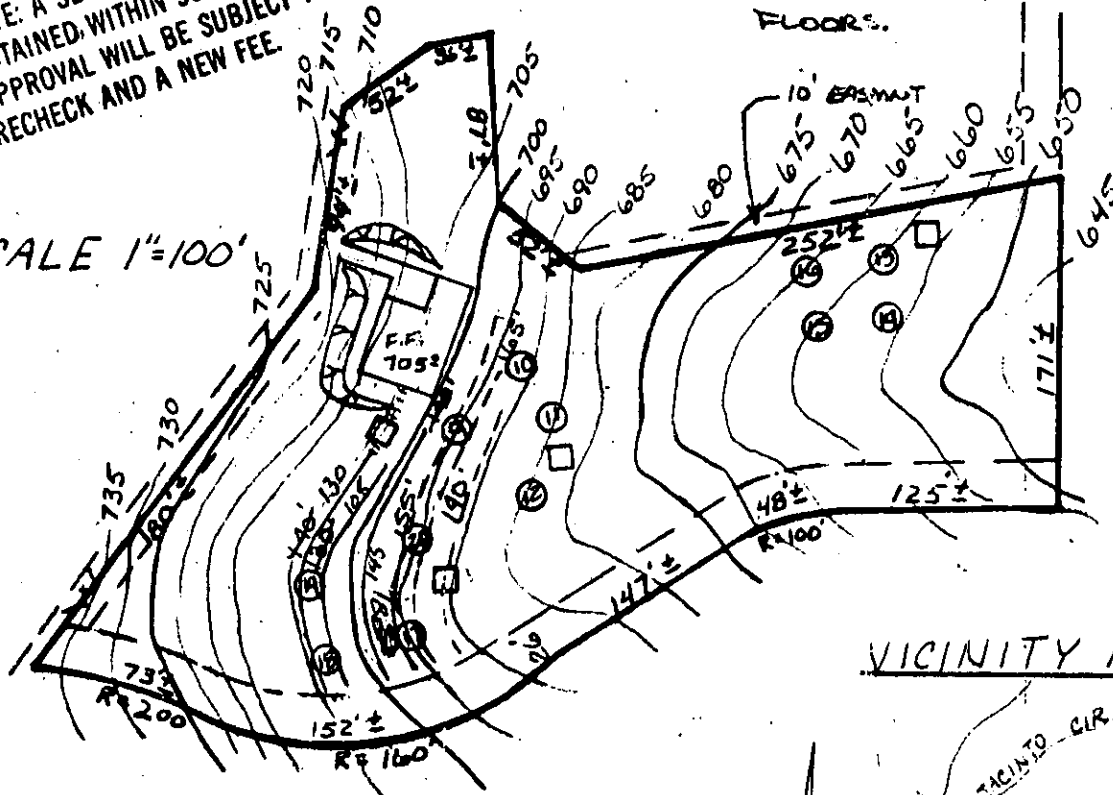

VICINITY MAP

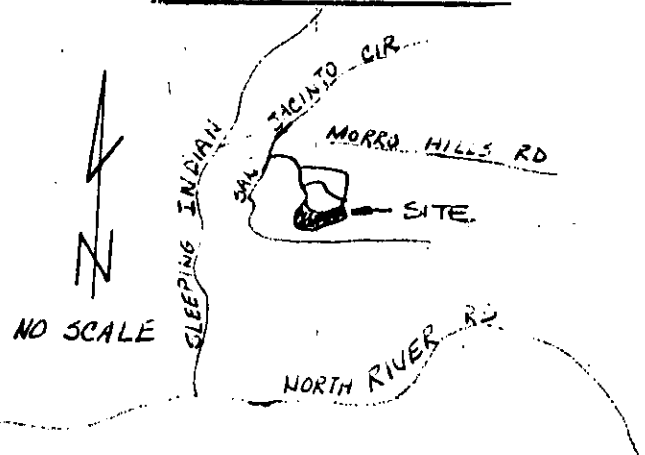

NOTE - 5' PERC TEST
3' Rock under 7.5' layer
1" PE.

This approval will be VOID unless the Structures, Driveway, and Grading are located as shown and the Leach Lines or Seepage Pit(s) are located exactly as shown on this plan. Any proposed change shall be approved by the Dept. of Health Services prior to beginning construction, and may require additional soil testing.

Plot plan as shown by engineer is in substantial compliance with County Code.

Sanitarian

John Coston

COUNTY OF SAN DIEGO DEPARTMENT OF PUBLIC HEALTH
1600 PACIFIC HWY, SAN DIEGO, CA 92101
PHONE: 236-2243

Job #1106-81

Mr. Terry Williams

Test Results - Off San Jacinto Circle, Sleeping Indian area,
Fallbrook, California.

<u>Test No.</u>	<u>Depth of Hole</u>	<u>Safety Factor</u>	<u>Time/Inch</u>
9	5 feet	1	50
10	5 feet	1	50
11	5 feet	1	48
12	5 feet	1	34
13	5 feet	1	20
14	5 feet	1	26
15	5 feet	1	50
16	5 feet	1	30

Average = 39 minutes per inch



This is a copy of the original document. It is not to be used for legal purposes. This is a copy of the original document. It is not to be used for legal purposes.
