

Lic#1009043

PO BOX 3357 PASO ROBLES CA 93447 805-221-5493

## Inspection/Certification

Date of Inspection: 10/02/2025 Property Owner: Debi Ferrante

Inspection Address: 2015 Calle Pattito, Templeton CA 93465

Realtor/Finance Company: David Crabtree

Title Company: N/A

I examined the existing septic system at the location above and determined:

Septic tank capacity: 1500

Septic tank construction: Concrete

Liquid level in tank: Good

Condition of tank: Good

Effluent filter present: No

Septic tank construction: Concrete

Gravity/Pump system: Gravity

Condition of internal piping: Good

Condition of access lids: Good

Septic tank pumped during inspection: Yes

Back flow from leach field before or after pumping septic tank: No

Operational leach field 300-gallon water test: Passed

Setback issues from dwellings, wells, or natural water courses: None

Evidence of surfacing effluent found on property: No

Comments: Septic tank should be serviced every 3-5 years.

X: It is my opinion that, as of now, the septic system appears to be in good working order and can be expected to function correctly with proper maintenance. No repairs are needed at this time.

: It is my opinion that, as of now, the septic system is NOT in good working order and will NOT function properly without the following repairs:

Brian Padgett - Alliance Septic Service


- \* The results of this inspection in no way guarantee future function of the septic system or its components. Future functionality will depend on proper usage, environment, and maintenance.
- \* This inspection is good for 90 days.
- \*Color and texture of soil may look different upon completion over excavated/graded areas.
- \* Sewer pipes from the building(s) to the wastewater system, and greywater diversions of any kind are not included in this inspection.
- \*Soil color and texture may look different upon completion of work. Rocks/boulders may be visible at ground surface.




Lic# 1009043
Date: \_ iの2125

Address:	2015	CALLE	PATHO	TEMPL	ETON
Comments:	1500	GALLO	V CON	CRETE	TANK
UM	ider L	HNOSCA	, DE	· · · · · · · · · · · · · · · · ·	V

Y Full Diameter Access Risers to Grade Depth From Top of Tank to Grade 40 ''

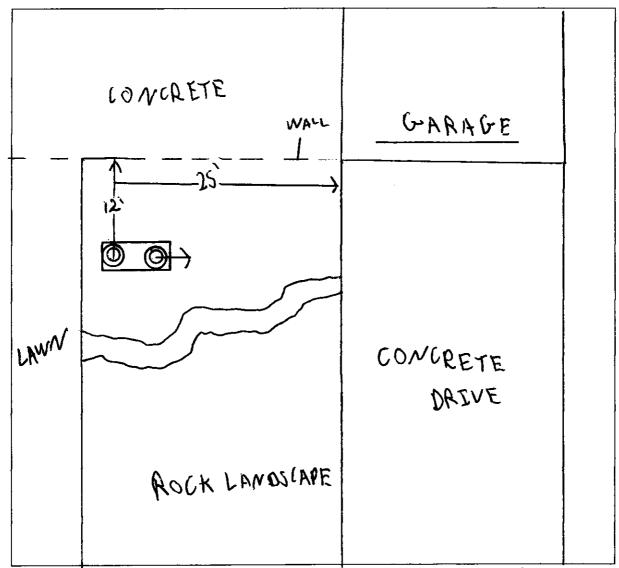

Locations shown are approximate. Exact locations and scales are not within the scope of this inspection



## **Invoice**

Date	Invoice #
10/6/2025	7332

Due Upon Receipt

Bill To	06 20	
ebi Ferrante	10/0	
015 Calle Pattito		

Debi Ferrante 2015 Calle Pattito Templeton, CA 93465

P.O. No.

**Project** 

Quantity	Description	Rate	Amount
1	Escrow inspection on a 1500 gallon septic system- 2015 Calle Pattito, Templeton	200.00	200.00
1	Septic tank pumping (up to 1200 gallons)	595.00	595.00
300	Overage (1500 gallon septic tank)	0.35	105.00

There will be an additional \$25 service fee, plus bank fees, added for declined payments.

**Total** \$900.00

Phone #

8052215493

E-Mail alliancesepticservice@gmail.com Payments/Credits -\$900.00

**Balance Due** 

\$0.00
